



# Vertical Platform Lift

Jobsite Preparation  
Checklist

  
**AmeriGlide**  
ACCESSIBILITY SOLUTIONS

5110 Atlantic Ave. Raleigh, NC 27616 | 1-800-790-1635 | [AmeriGlide.com](http://AmeriGlide.com)




146\_AMG VPL\_JobsitePrepChecklist\_032824

### 1 Upper Landing Gate

Ensure to have solid beams on each side of the gate to properly secure it.

Below is the space required. For instance, a 36" wide gate requires 44 1/4" (see highlight).

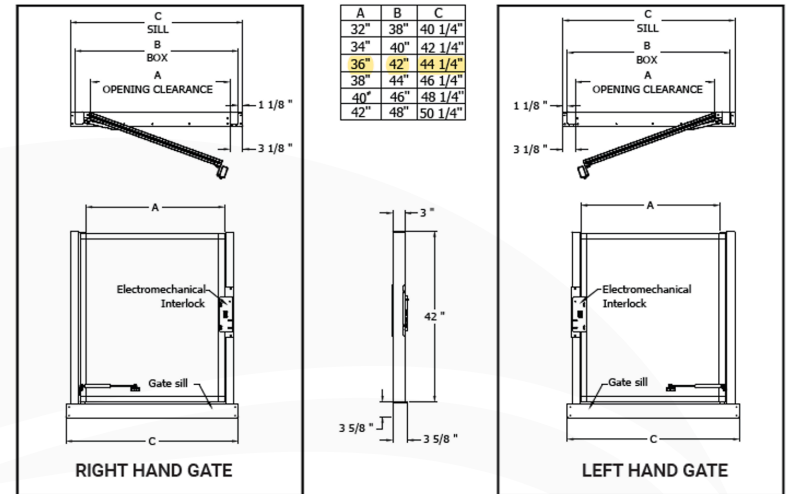

### 2 Protection Wall

Smooth surface without pinch points from the ground to the first level and must extend 12" on each side of the vertical platform lift.

### 3 Electrical Outlet

Power supply must be 120 volts / 20 amps.

Needs to be a maximum 10ft within the vertical platform lift location.



**IMPORTANT: ALL WORK AND MATERIALS MUST COMPLY WITH ALL LOCAL LAWS AND REGULATIONS.**



#### ④ Concrete Slab

7' L x 5' W x 6" D

Minimum of 25 MPA/ 3625 PSI to support 1500 lbs loads.

May need to be winterized depending on location.

#### ⑤ Lifting Height

Confirm height from concrete pad to 1st floor.



LIFTING HEIGHT

**IMPORTANT: ALL WORK AND MATERIALS MUST COMPLY WITH ALL LOCAL LAWS AND REGULATIONS.**



# Jobsite Preparation Checklist

Name: \_\_\_\_\_

Address: \_\_\_\_\_

Phone Number: \_\_\_\_\_

**Please ensure there are no obstacles for the technicians**

### Requirement Checklist:

- 1. Upper landing gate (required space and structure)
- 2. Protection wall (remove if installed)
- 3. Electrical outlet (120V/20A) is installed
- 4. Concrete slab (7' L x 5' W x 6" D) is installed
- 5. Lifting height measurement

### Please provide the following photos:

- The concrete slab
- The protection wall
- The electrical outlets
- From the upper landing (side railings)

Notes: \_\_\_\_\_  
\_\_\_\_\_  
\_\_\_\_\_

I hereby certify that the information provided on this form is true and accurate. Any discrepancies that require the install crew to delay or leave the job site will incur a minimum \$1,500 redeployment fee (Travel expenses will be extra) and must be paid in advance.

Signature: \_\_\_\_\_

Date: \_\_\_\_\_

Builder/Homeowner Representative Signature
